

073105T4ARC

ARCHITECTURAL DRAFTSMANSHIP LEVEL 5

CON/OS/ARC/CR/04/5/

Install Building Finishes and Fittings

July/ August 2025



**TVET CURRICULUM DEVELOPMENT, ASSESSMENT AND CERTIFICATION
COUNCIL (TVET CDACC)**


**PRACTICAL ASSESSMENT
TIME: 6 HOURS**

INSTRUCTIONS TO CANDIDATE

1. You are required to perform the following practical tasks
 - i. *TASK 1: Identify and prepare a plastered surface for wall tile installation*
 - ii. *TASK 2: Mark 1200mm x1200mm on the plastered surface.*
 - iii. *TASK 3: Install the wall tiles as shown in the attached plan drawing A*
2. You are provided with the following resources:

Tools/Equipment	Materials
<ul style="list-style-type: none">• Cold chisel• Scrub brush• Brush comb• Serrated Trowel	<ul style="list-style-type: none">• Lime• Grout• Gloves• Water

<ul style="list-style-type: none">• Shovel• Masons Square• Masons Trowel• Tile cutter• Tile spacers• Paint bucket• Builders line• Spirit level• Setting out pegs• Tape measure	<ul style="list-style-type: none">• Masking tape• Steel wool• Markers/pens• One (1) Wheelbarrow of Clean River sand• 20 pieces of ceramic tiles (300x300)
---	---

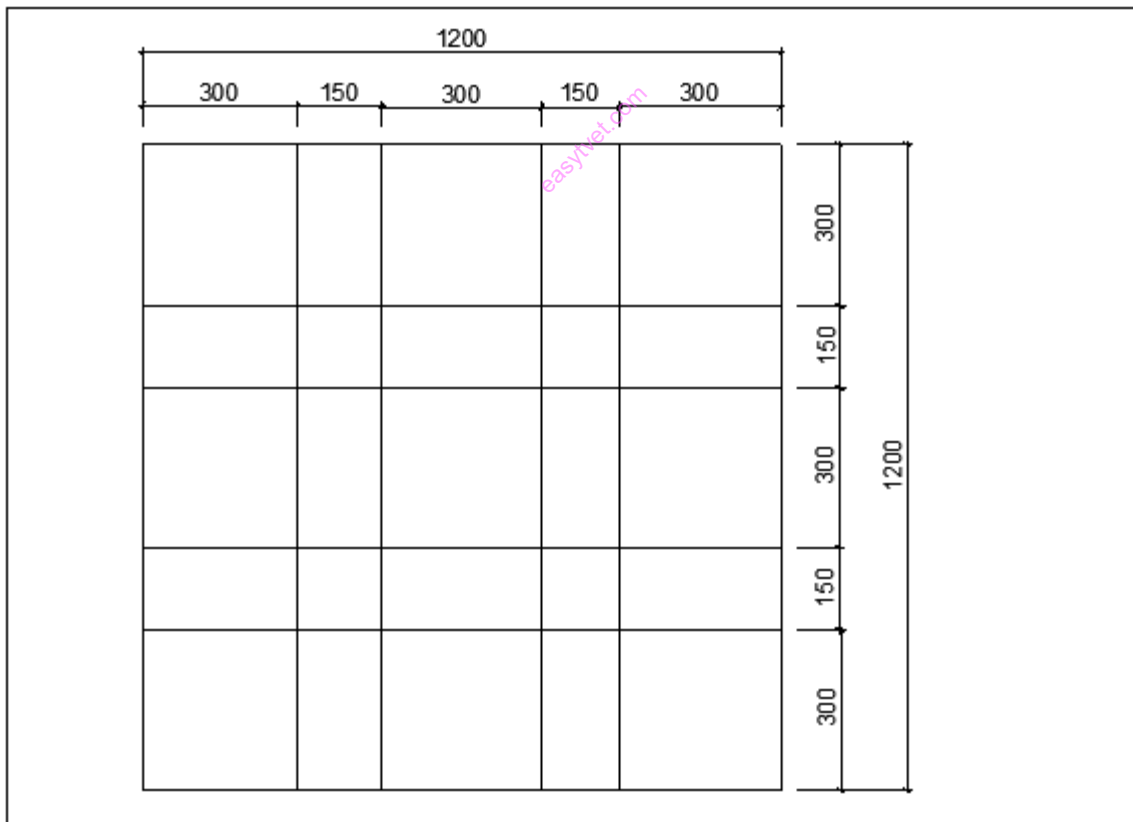

Drawing A.
