

073206T4BLD

BUILDING TECHNICIAN LEVEL 6

CON/OS/BUT/CR/05/6

Execute Substructure Works

July/August 2025



**TVET CURRICULUM DEVELOPMENT, ASSESSMENT AND CERTIFICATION
COUNCIL (TVET CDACC)**

PRACTICAL ASSESSMENT

Time: 5 HOURS

INSTRUCTIONS TO CANDIDATE:


1. You are required to perform the following tasks
 - i. Set out using 3-4-5 method the provided working drawing, fix profile boards and mark excavation lines.
 - ii. Install foundation walling formwork of 6" x 1" along one width and half-length of one side
2. You have been provided with the following resources for the practical tasks:

S/N	Tools/Equipment	Materials
1.	Tape measure	Profile boards timber 2" x 2"
2.	Claw hammer	6" x 1" timber
3.	Builders' line	Pegs
4.	Mason Square	Lime
5.		2" nail

Working drawing



Formwork drawing

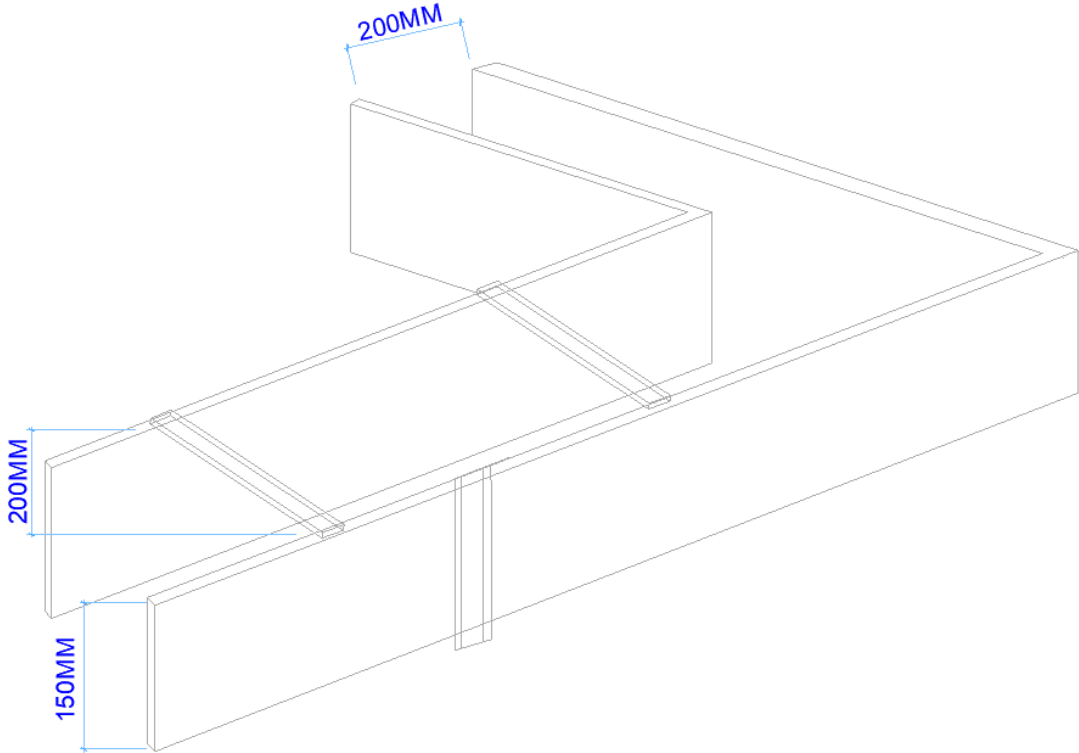

easyvet.com
